

Tyger River Elementary School





Tyger River Elementary School

















Wellford Academy of Science and Technology





Wellford Academy of Science and Technology

Bus Loop

- Paving and striping are complete
- Excess soil stock piled and to be moved to the Byrnes Stadium project
 - Approximately 2 months

Marquis sign

• Installed and operational

Punch List

• Nearing completion



Upcoming

 Grassing the field once stockpile is removed



Abner Creek Middle School





Abner Creek Middle School











Beech Springs Middle School – Practice Field





Beech Springs Middle School – Practice Field

Upcoming

- Second round of sanding, fertilizing, aeration, and rolling scheduled for 8/29 – 8/30
- Storage building trim work to be installed
- Final inspection on Friday





Beech Springs Middle School – DOT Improvements

Ongoing

- Owners appraisals are complete
- Right-of-way easement offer letters
 mailed to property owners last week

Upcoming


 Upon agreement with property owners, cross-sections of disturbed portions within easements will be drawn and issued to Spartanburg County for final review process









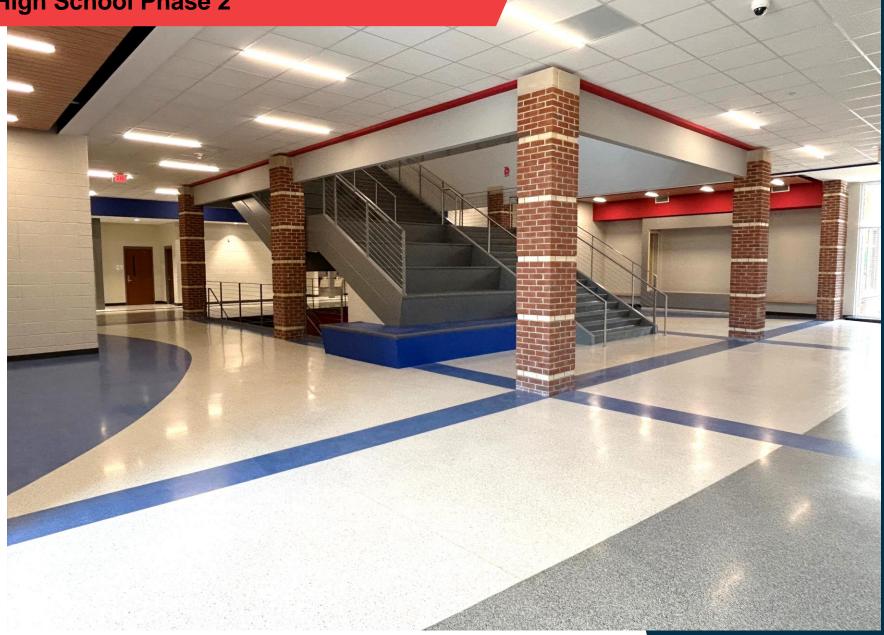












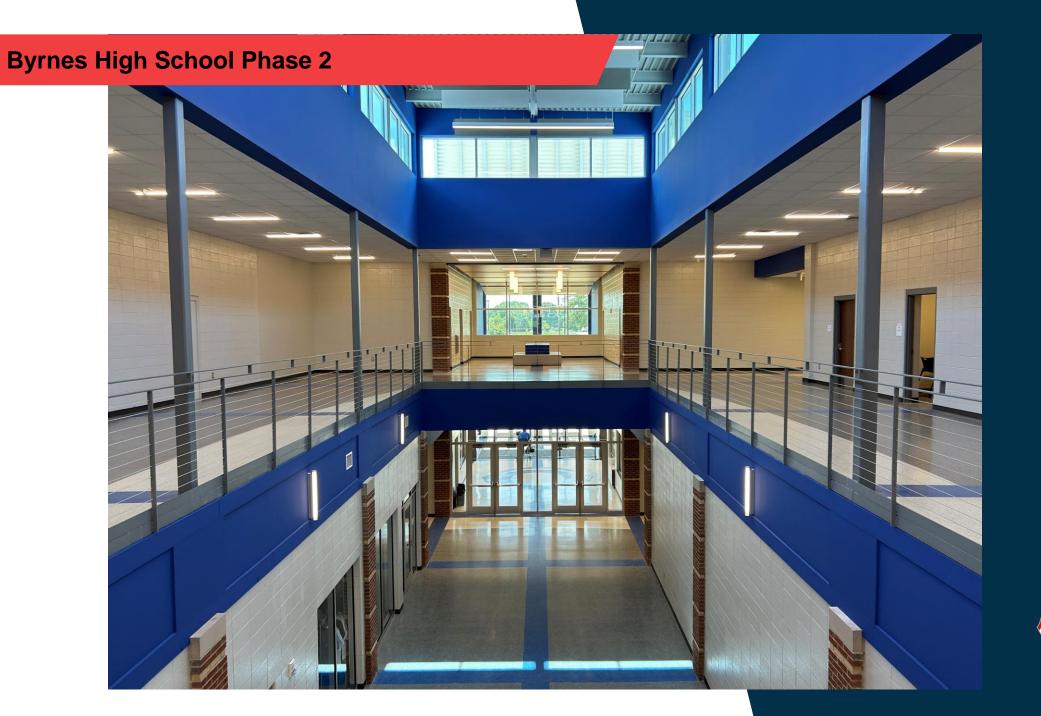



Upcoming

- Punch list completion for half of the building is on going
- Punch list for the remaining half is scheduled for 8/28 & 8/29
- Display cases scheduled to be completed this week





Completed


- Abatement of former front office side
- Temporary canopy footings installed

Upcoming

- Abatement of Fine Arts side to be completed in two weeks
- Construction fencing 9/6
- Temporary canopy to band building 9/9
- Retaining wall behind Fine Arts to begin mid-late September
- Demolition of former front office side to be complete by the 2nd week of October
- Demolition of Fine Arts side to be complete by the 1st week of November







Byrnes High School Stadium









Byrnes High School Stadium





Byrnes High School Stadium

Completed

- All demolition
- Temporary student access
- Building pads at grade

Upcoming

- Footings for Press Box building began today
- Footings for remaining home side buildings to begin on 9/9
- Press Box slab on grade 9/23



Retaining wall for switch-back ramp on visitors side to begin in 2 weeks



