




Facilities Updates
05/19/25

Byrnes High School Phase 3 – Areas G & H



Areas G & H

- 2nd floor joist install is complete
- 2nd floor decking is nearing completion
- 2nd floor concrete slab pour scheduled for this week
- 2nd floor masonry wall construction to begin next week
- Cafeteria patio demolition begins next week



Byrnes High School Phase 3 – Areas D & F




Area D

- 2nd floor joist install is nearing completion
- Floor decking to begin this week
- 2nd floor concrete slab pour scheduled for next week

Area F

- 1st floor masonry walls are complete
- 2nd floor joist install begins this week




Byrnes High School Phase 3 – Area E



Area E

- Retaining wall backfill is complete
- Storm drain is nearing completion
- Building pad will be set at the end of the week
- Footings to begin in two weeks


Schedule is on track




Byrnes High School Stadium




- Reserved seating, handrails, and guardrails are complete
- Light poles have been installed
- Metal roofing installation is in progress



Byrnes High School Stadium

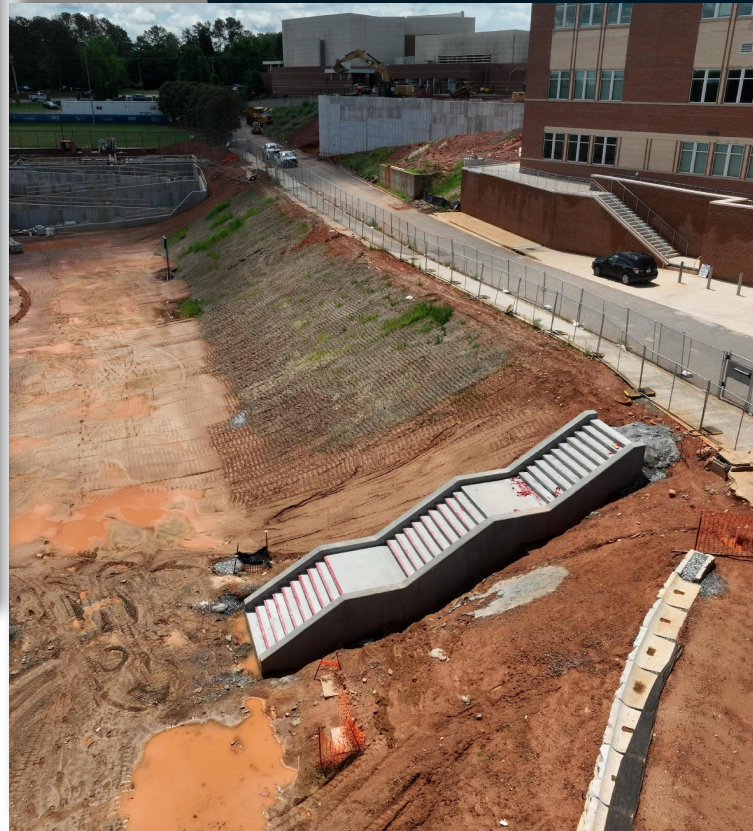


- Track Storage & Locker Room building – Exterior finishes and roofing are in progress
- Building will be in the dry this week
- Stairs for field access are nearing completion



Byrnes High School Stadium



- Home concourse area is taking shape –
Brick columns
Lighting
Exterior finishes
- Home plaza ramp and stairs are in progress




Byrnes High School Stadium



- Press Box interior – cabinets to be installed this week
- 2-Story stair to be poured end of May
- Home restroom buildings will have plumbing fixtures installed over the next 2 weeks
- Visitor bleachers had their final pour today
- Visitor Concessions building will be in the dry this week

Schedule is on track





Questions
