



Facilities Update 9/26/22



Construction Projects



EVERY CHILD, EVERY DAY.

BHS Phase 2



Current:

- Silt fence installation
- Demo existing storm drains
- Building pad preparation



BHS Phase 2



Upcoming:

Begin installation of :

- Building pads and footings
- New storm drains
- Sanitary sewer lines





EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.

Beech Springs



Current

- Permit acquisition delaying schedule
- Jobsite trailer installed



Beech Springs



Upcoming:

- Temporary canopy at admin entrance
- Temporary office casework
- Sitework to begin after permit recd.




mcmillan | pazdan | smith
ARCHITECTURE

BEECH SPRINGS MIDDLE SCHOOL
SPARTANBURG COUNTY SCHOOL DISTRICT FIVE
200 DANZLER RD,
DUNCAN, SC 29334

FRONT ENTRY PERSPECTIVE

05/17/22

EVERY CHILD, EVERY DAY.

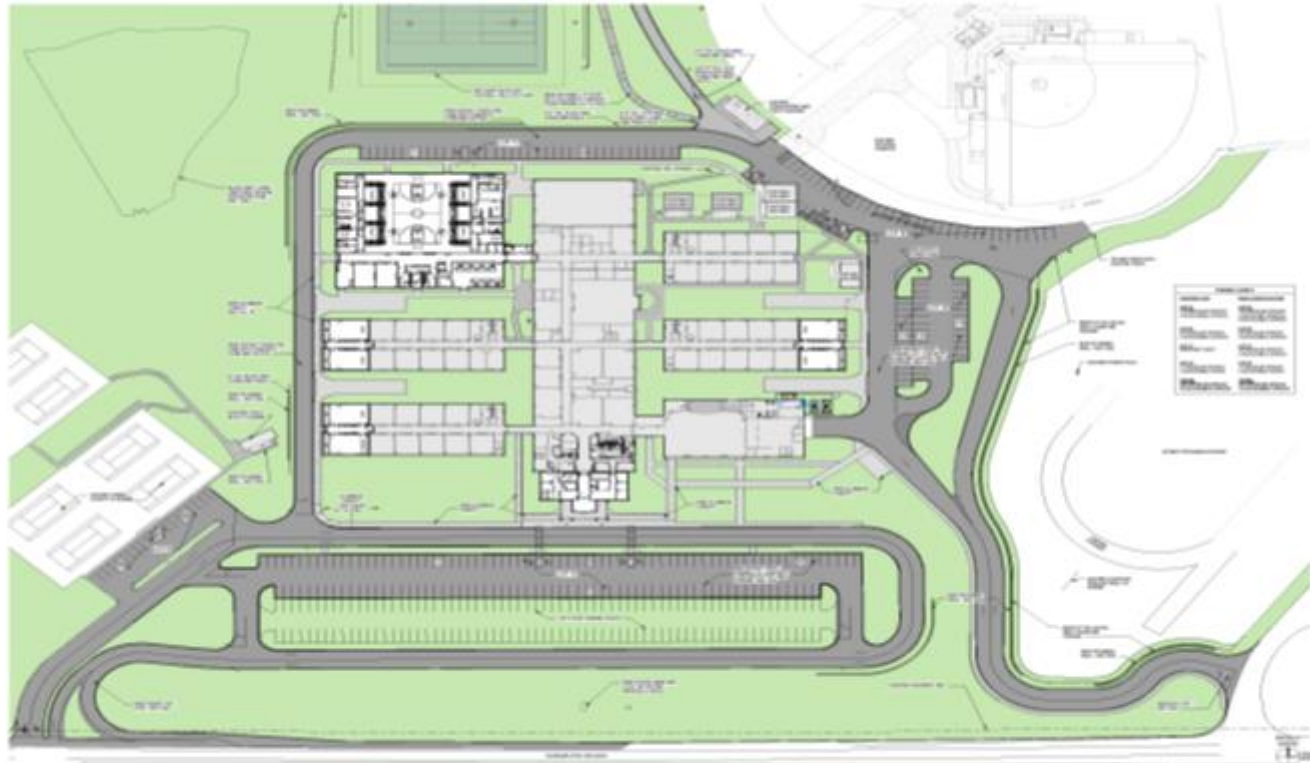

 **mcmillan | paadan | smith**
ARCHITECTS

BEECH SPRINGS MIDDLE SCHOOL
200 SANDLER RD.
BEECH SPRINGS, AL

ARCHITECTURAL SITE PLAN

EVERY CHILD, EVERY DAY.

Berry Shoals



Classroom Wing:

- Roofing dry-in complete
- Mechanical and electrical overhead rough-ins complete
- Ceiling grid install to begin 9/26/22

Berry Shoals



Kindergarten Renovation:

- Overhead electrical and mechanical rough-ins complete
- Interior/exterior block walls complete





EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.

New Elementary (Hwy 29)



Current:

- Tree and brush removal complete
- Storm drain installation ongoing
- Retention ponds installed and seeded
- Hwy. 29 entrance graded and installed

New Elementary (Hwy 29)



Upcoming:

- Grade building pad
- Install concrete foundations
- Begin underground utilities
- Install temporary jobsite fencing
- Coordinate utility service





EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.

Reidville Elementary Addition



Current:

- Building pads graded
- Storm drains complete
- Fire lane installed
- Playground relocated
- Bus loop fencing installed



Reidville Elementary Addition



Upcoming:

- Begin concrete foundations
- Begin underground utilities





EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.

Reidville Elementary Crosswalk



EVERY CHILD, EVERY DAY.

New Wellford Academy



Current:

- Bidding early site package
- Construction Design Phase ongoing
- Due diligence on Porter Street parcel



EVERY CHILD, EVERY DAY.


New Wellford Academy



Upcoming

- Oct. 17, 2022: Early Site GMP
- Nov. 21, 2022: Building GMP



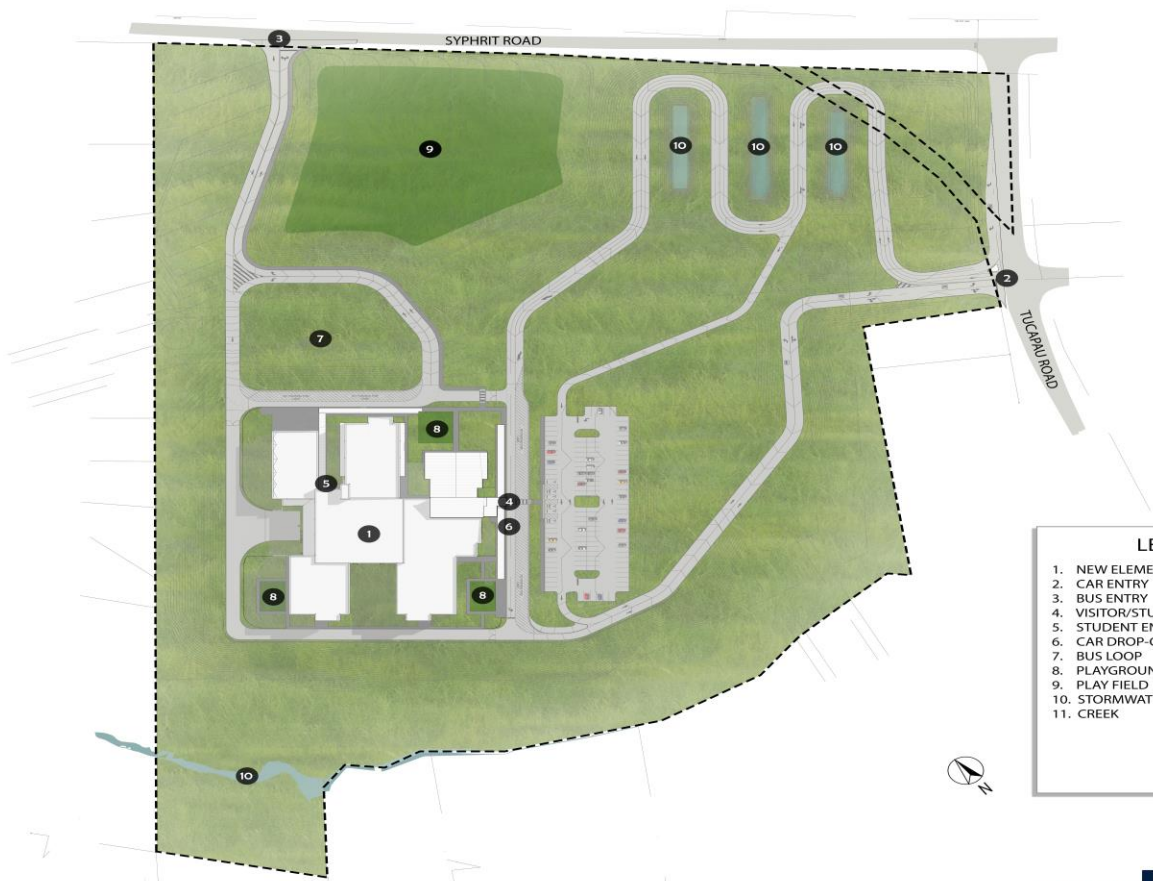

- LEGEND**
- 1. NEW ELEMENTARY SCHOOL
 - 2. CAR ENTRY
 - 3. BUS ENTRY
 - 4. VISITOR/STUDENT ENTRANCE (CAR)
 - 5. STUDENT ENTRANCE (BUS)
 - 6. CAR DROP-OFF
 - 7. BUS LOOP
 - 8. PLAYGROUND
 - 9. PLAY FIELD
 - 10. STORMWATER RETENTION BASIN
 - 11. CREEK

08/29/22

AP-AS3 COLORED SITE PLAN



EVERY CHILD, EVERY DAY.

Hwy. 296 and Pine St. Signal



- July 1, 2022: Project bid to SCDOT approved contractors
- Aug. 2022: Project issued to Walker Brothers (\$ 126,310)
- Feb. 2023: Signal installation begins

New Abner Creek Middle School



Current:

- All structural steel erected
- Roof drain installation
- Locker rooms and concessions walls erected
- Slab, underground utilities and overhead mechanical installation ongoing throughout



EVERY CHILD, EVERY DAY.



EVERY C



EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.

