



# Facilities Update 4/22/24



# Construction Projects



EVERY CHILD, EVERY DAY.

# Byrnes Phase 2




**EVERY CHILD, EVERY DAY.**



**EVERY CHILD, EVERY DAY.**





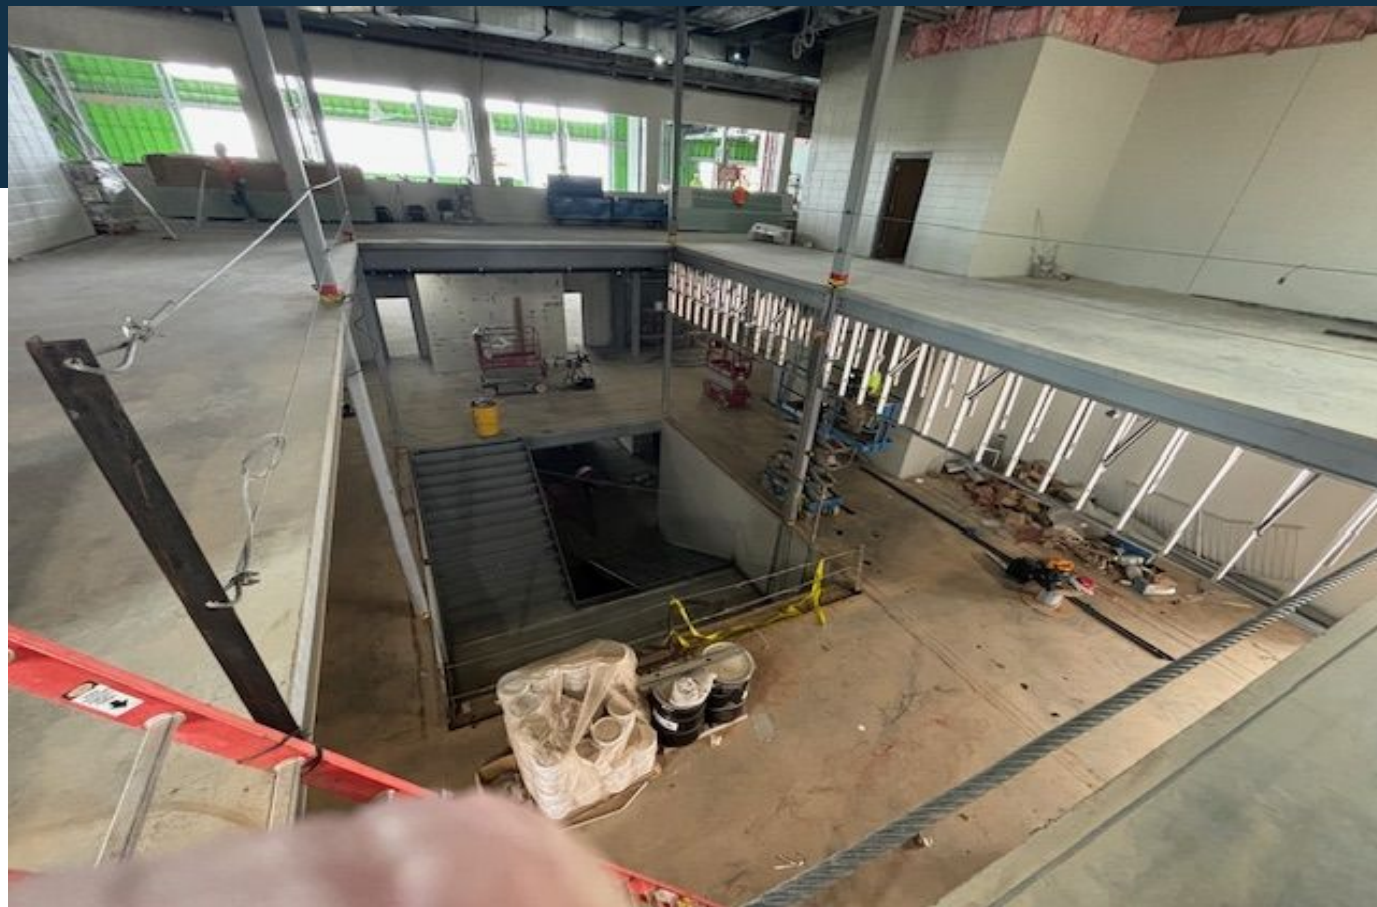

**EVERY CHILD, EVERY DAY.**



**EVERY CHILD, EVERY DAY.**





**EVERY CHILD, EVERY DAY.**







**EVERY CHILD, EVERY DAY.**





**EVERY CHILD, EVERY DAY.**



# Byrnes Phase 2



## Complete:

- Exterior brick (stadium side)
- Admin epoxy floor installation
- Admin plumbing fixtures set
- Cooling tower set April 4



# Byrnes Phase 2



## Ongoing:

- Main stair installation
- Admin drop-ceiling installation
- Exterior Finish (Danzler Rd. side)
- Classroom building sidewalks
- Drywall installation (classroom bldg.)

# Byrnes Phase 2



## Upcoming:

- Classroom bldg. ceiling grid install
- Air conditioning start-up 5/12/24
- Furniture delivery 7/15/24
- OSF Final Inspection (TBA)





# Beech Springs Gym



**EVERY CHILD, EVERY DAY.**





**EVERY CHILD, EVERY DAY.**

# Beech Springs Gym



## Complete:

- Display case installation

## Ongoing

- Emergency signal relay installation

## Upcoming

- Final Inspection 5/1/24





# New Beech Athletic Field



EVERY CHILD, EVERY DAY.





# Danzler Rd. Improvements



## Ongoing:

- Easement/right-of-way process



# New Beech Athletic Field



## Complete:

- Field grading
- Storage building slab

## Ongoing

- Spreading topsoil
- Removal of existing lighting



# New Beech Athletic Field



## Upcoming:

- Irrigation installation
- Underground electrical for lighting & scoreboards
- Begin use 8/1/24



# New Tyger River Elementary



**EVERY CHILD, EVERY DAY.**







**EVERY CHILD, EVERY DAY.**





**EVERY CHILD, EVERY DAY.**



**EVERY CHILD, EVERY DAY.**





**EVERY CHILD, EVERY DAY.**





**EVERY CHILD, EVERY DAY.**





**EVERY CHILD, EVERY DAY.**





**EVERY CHILD, EVERY DAY.**

# New Tyger River Elementary



## Complete:

- Exterior fencing & sod
- Playground installation
- DHEC kitchen inspection 4/9 (target)
- OSF Final 4/30/24

# New Tyger River Elementary



## Ongoing:

- Wood door installation
- Bank re-stabilizing
- Camera, access control device install
- Cafeteria AV equipment install
- Boulevard & drive paving

# New Tyger River Elementary



## Upcoming:

- Gym floor installation
- Boulevard speed table install
- Landscaping
- Pavement striping 4/29/24
- Final OSF Inspection @ 4/30/24
- Furniture delivery 5/6/24





# New Wellford Academy



EVERY CHILD, EVERY DAY.



**EVERY CHILD, EVERY DAY.**





**EVERY CHILD, EVERY DAY.**

# New Wellford Academy



## Complete:

- Light fixtures
- Casework installation 95%

## Ongoing:

- Canopy installation
- Exterior metal wall panels
- Pour sidewalks



# New Wellford Academy



## Upcoming:

- Kitchen equipment installation
- Terrazzo floor install
- Final OSF Inspection @ 7/11/24
- Furniture delivery 7/15/24





# Misc. Projects



**EVERY CHILD, EVERY DAY.**

# Abner Creek Middle School



- Furniture delivery scheduled for 4/29/24



# BHS Stadium Replacement



- Construction GMP 5/20/24



# Berry Shoals Elementary School



- Playground install begin 4/22/24
- Carpet Kg rooms June 2024



# Byrnes Phase 3



- Demo phase GMP 4/22/24
- Construction phase GMP 7/29/24





# Duncan Elementary School Roof Replacement



- Project is 70% complete
- Currently 16 rain days
- Completion scheduled for 7-19-24



# Summer Internal/External Moves



- District-wide, 186 teachers moving externally
- BHS has 46 + moving internally
- WA has 43 moving from old to new school
- Moving company & D5 movers
