



Facilities Update 2/26/24



Construction Projects



EVERY CHILD, EVERY DAY.

Byrnes Phase 2



EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



Byrnes Phase 2



Complete:

- Power connected in admin. 1/30/24
- Admin overhead inspection 1/31/24
- Classroom bldg. in dry 2/10/23
- Rooftop air units set 2/15/24
- Exterior sheathing 2/16/24
- BHS faculty tours 2/16/24



Byrnes Phase 2



Ongoing:

- Classroom bldg. exterior brick
- Admin. casework installation
- Admin terrazzo began 2/19/24

Upcoming:

- Window Installation begins 3/11/24
- Classroom bldg. completion 8/1/24

Beech Springs



EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.



Beech Springs Gym



Ongoing:

- Gym floor

Complete:

- Tile flooring
- Restroom fixtures
- Recess area



Beech Springs Gym



Upcoming:

- Bleachers install 2/26
- Final Inspection @ 3/4/24



New Tyger River Elementary



EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



New Tyger River Elementary



Complete:

- Roof
- Heat/ conditioned air
- Traffic signal operational 2/14/24
- Exterior lighting



New Tyger River Elementary



Ongoing:

- Terrazzo flooring
- Casework
- Ceiling grid (K-2)
- Sod preparation



New Tyger River Elementary



Upcoming:

- Playground delivery 3/4/24
- Final overhead inspection 3/6/24
- Playground eqpt. delivery 3/11/24
- Final OSF Inspection @ 4/11/24
- Furniture delivery 5/6/24

New Wellford Academy



EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.





EVERY CHILD, EVERY DAY.



EVERY CHILD, EVERY DAY.



New Wellford Academy



Complete:

- Building energized 2/1/24

Ongoing:

- Ceiling grid began 2/12/24
- Casework began 2/5/24
- Metal roof installation



New Wellford Academy



Ongoing (cont.)

- Sheetrock installation
- Overhead installation

Upcoming:

- Playground delivery 3/4/24
- Furniture delivery TBA
- Permanent heat to begin 3/4/24
- Final OSF Inspection @ 7/11/24



New Beech Athletic Field



- OSF building permit received 2/9/24
- Awaiting county site permit
- Ease/right-of-way process ongoing




Misc.



- ACMS furniture delivery 4/29/24



Byrnes High School Stadium

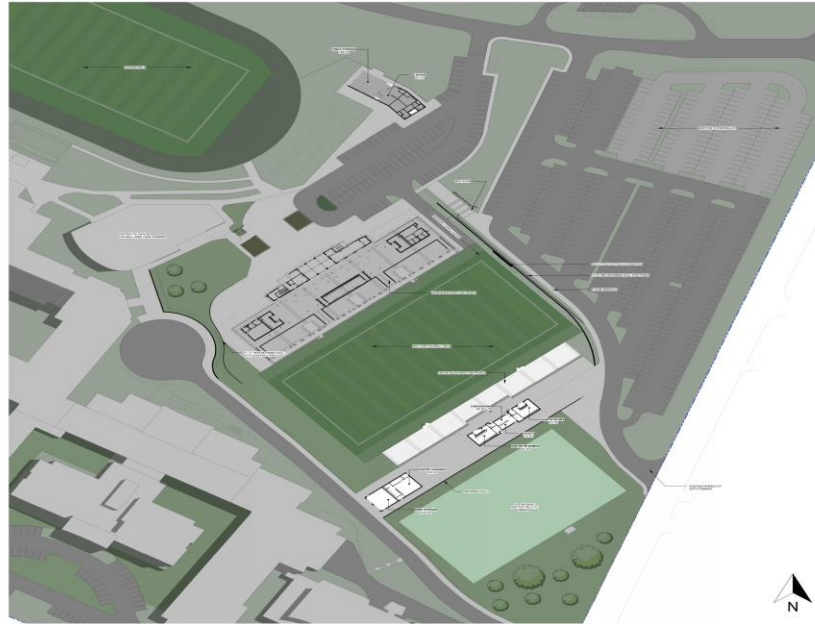

 **mcmillan | pazdan | smith**
ARCHITECTURE

BYRNES HIGH SCHOOL FOOTBALL STADIUM
150 E Main St
Duncan, SC 29334
06.26.2024

SPARTANBURG DISTRICT **Five**
EVERY CHILD. EVERY DAY.

SITE PLAN

EVERY CHILD, EVERY DAY.



BYRNES HIGH SCHOOL FOOTBALL STADIUM

150 E. Main St.
Durham, NC 27604
02.26.2024



FOOTBALL STADIUM AXON

EVERY CHILD, EVERY DAY.

