

Facilities Updates 06/23/25





## Areas G & H

- 2<sup>nd</sup> floor concrete slab has been poured
- 2<sup>nd</sup> floor masonry walls will be complete this week
- Roof joists will begin install
  1st week of July
- Roofing will begin at the end of July
- In-wall and overhead utilities are on-going
- Brick install will begin in August
- Cafeteria patio demolition is complete
- Cafeteria footings began today
- Front drive is being lowered and new retaining wall install will begin soon



#### Area D

- 2nd floor concrete slab has been poured
- 2nd floor masonry walls will be complete this week
- Roof joists will begin the second week in July
- Roofing will begin the 3rd week in July
- Brick install will begin at the end of July

#### Area F

- 2nd floor concrete slab has been poured
- 2nd floor masonry walls began last week
- Brick begins July 10th
- Roof joists will begin at the end of July



# Area E

- Area footings have been poured
- Foundation masonry will begin this week
- Underground utilities will begin the first week of July
- Slab on grade scheduled to be poured second week in July

Schedule is on track




- Concrete flat work is on-going
  working their way inside out
- Brick piers for fencing is nearing completion
- Home planters, ramp, and stairs complete in 2 weeks
- Visitor concrete flat work to begin next week
- Parking lot to begin July 1st
- Bleacher benches and stairs to be complete this week
- Brick masonry is complete on all but two buildings






- Turf install is on-going
- Rebels logo and letters are being cut in
- Final details and completion by July 1st



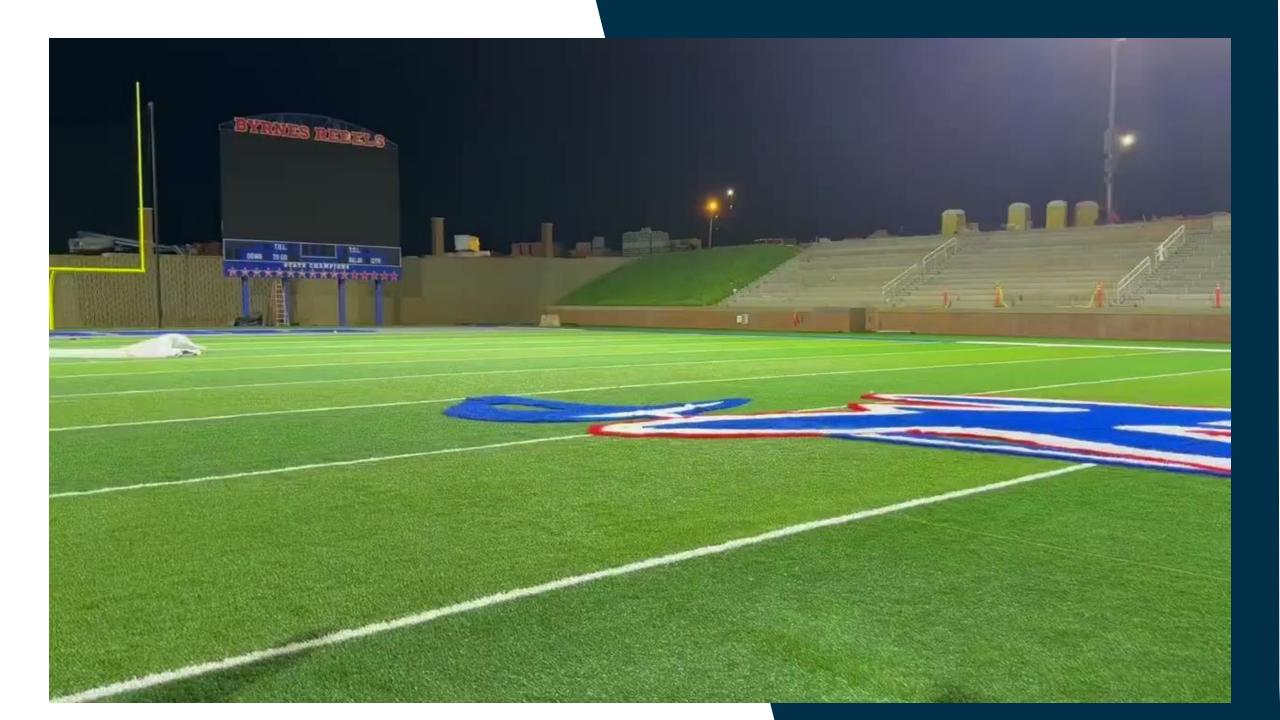

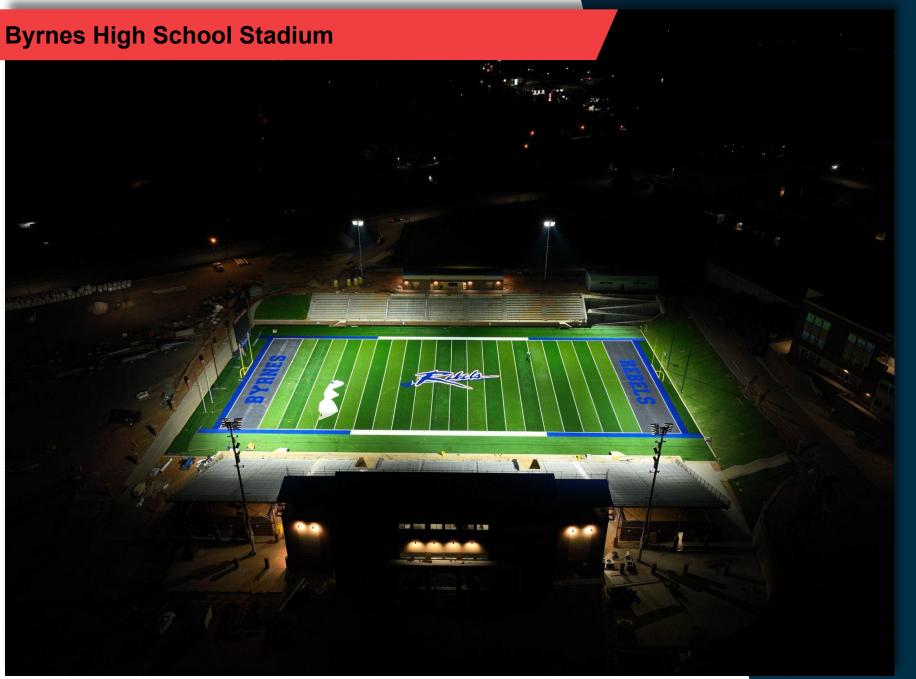

- Field lighting is now operational
- Lighting level adjustments are in progress
- Band field lighting is also in progress
- Parking lot lighting and pedestrian lighting will be installed



# **Byrnes High School Stadium**





- Home concourse area concrete is complete
- Home entrance concrete is on-going
- Plumbing fixtures in all home side buildings will be complete this week
- Press Box building interior only has floor finishes remaining
- Track/Locker building exterior finish and interior utilities are nearing completion
- Band building masonry and roof joists are complete
- Starting brick and roofing this week

Schedule is on track



## **Summer Capital Projects Update**

- Secure vestibule improvements to Lyman ES, Reidville ES, and Abner Creek Academy have begun
  - Tentative completion date of 7/22
- Concrete playcourts at Lyman ES, Reidville ES, and Abner Creek Academy began today
  - Tentative completion date of 7/18
- Byrnes Freshman Academy accessibility improvement project
  - Awaiting the arrival of the lifts
  - Tentative completion date of 7/30
- Lyman Elementary painting is complete
- Beech Springs and Florence Chapel classroom painting is on-going
- Byrnes Baseball scoreboard painting is complete
- River Ridge and Duncan Elementary Fire Alarm projects are ongoing
- Duncan Elementary fencing project to begin in July and have a two week duration



Questions
