

Facilities Updates 08/25/25





Areas G & H

- Roofing installation is in progress
- In-wall and overhead utility installation is in progress
- Brick installation to begin first week of September
- Cafeteria addition masonry wall construction will be complete this week
- Roof steel to begin this week
- New retaining wall on the front drive is complete



Area D

- High roof is dried in –
 began lower roof last week
- Brick installation is ongoing
- Overhead utility installation is ongoing

Area F


- Brick installation is complete
- Roof steel to begin after Area E floor steel



Area E

- Final slab on grade was poured last month
- Masonry wall construction is ongoing
- In-wall utility installation is ongoing
- Second floor steel framing to begin in September

Schedule is on track

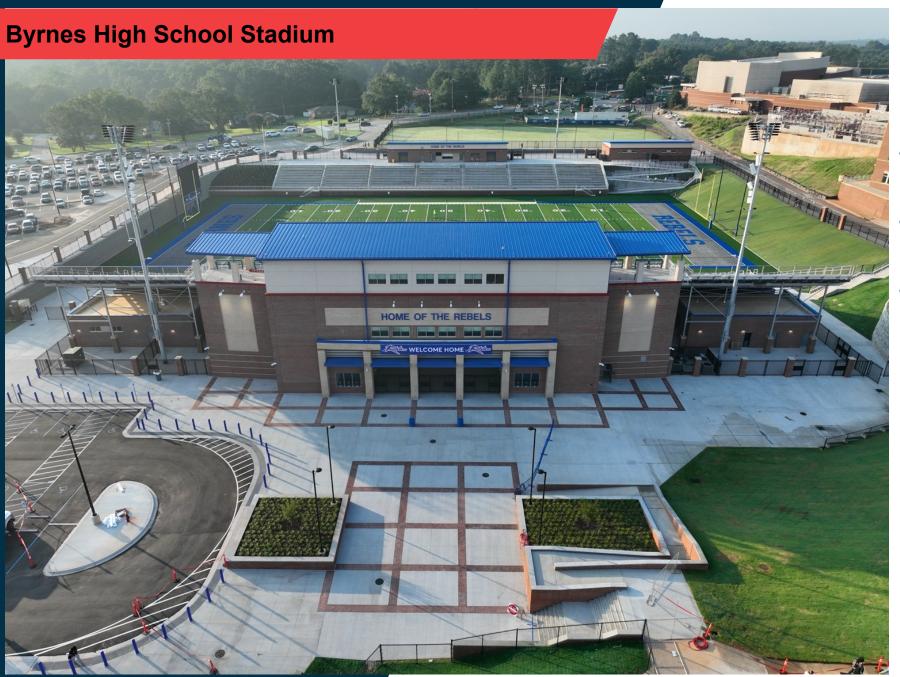


- Project has reached Substantial Completion!
- Received the Certificate of Approval from OSF
- Punch list with Thompson Turner has been created









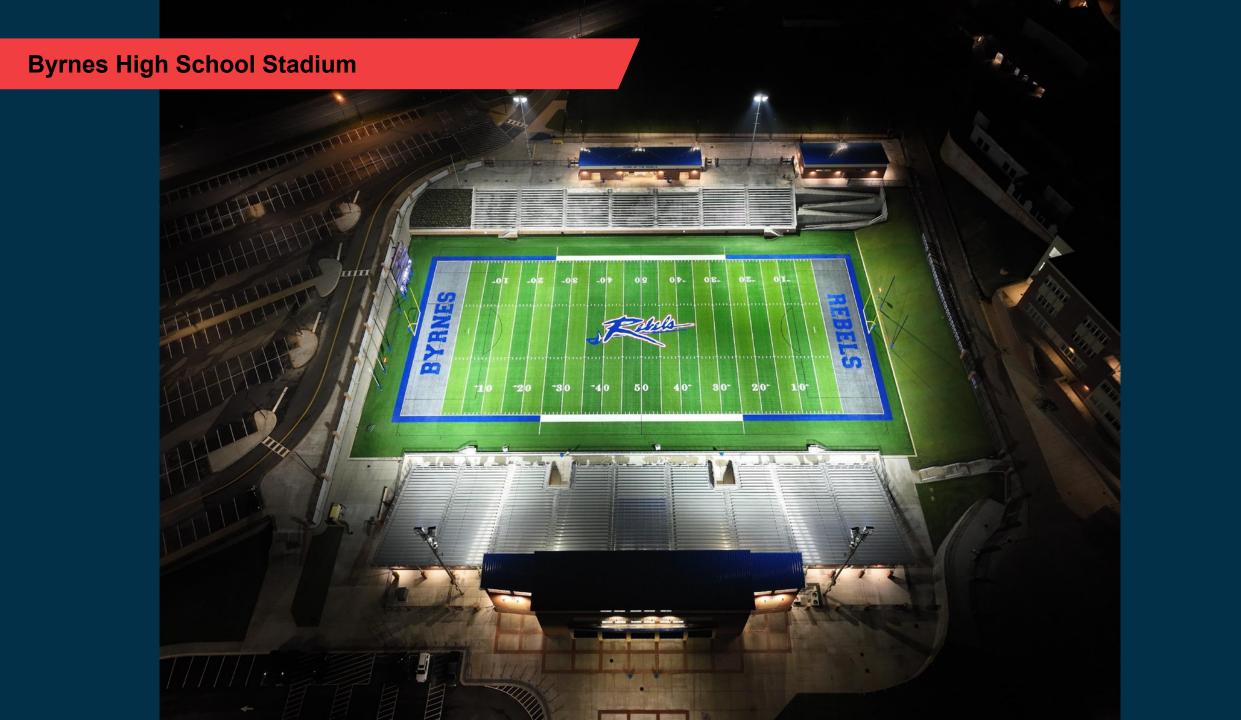




Secure vestibule improvements to Reidville ES, Abner Creek Academy, and Lyman ES are complete

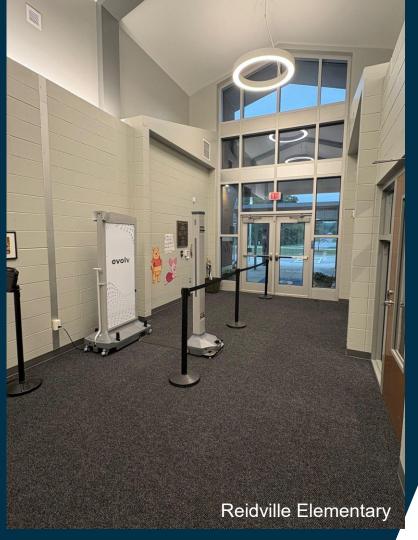


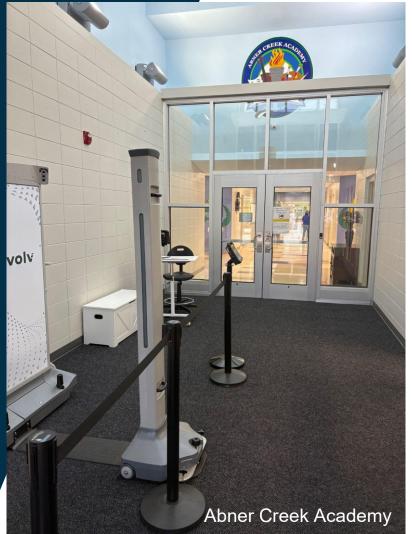

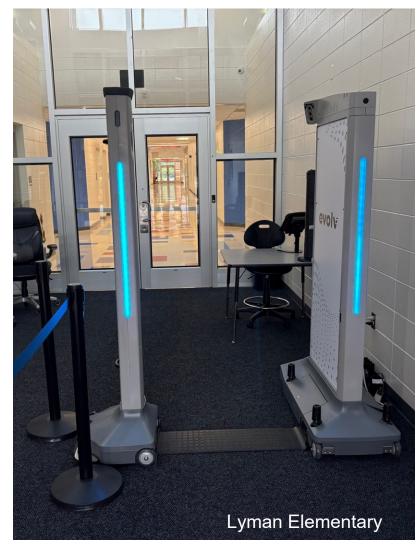


 Concrete playcourts at Reidville ES, Abner Creek Academy, and Lyman ES are complete



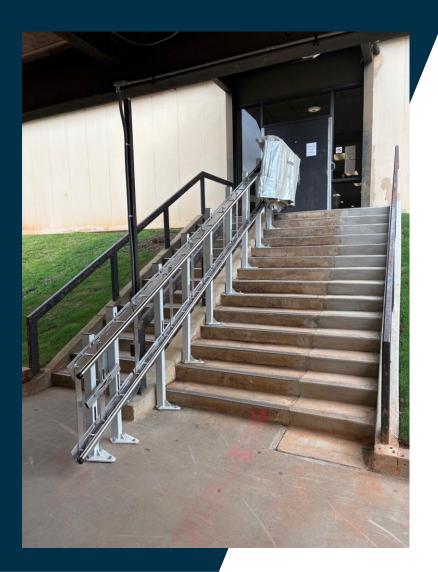

Byrnes Freshman Academy accessibility improvements

- Stair lift is complete
- Vertical lift is nearing completion

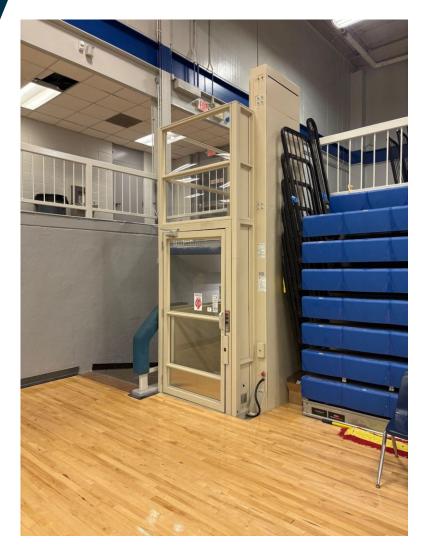



- Lyman Elementary, Beech Springs Middle, and Florence Chapel Middle painting is complete
- Byrnes Baseball scoreboard painting is complete
- River Ridge and Duncan Elementary Fire Alarm projects are complete
- Duncan Elementary fencing project is complete
- Various flooring replacement projects are complete
- Custodial team stripped and waxed over 1,000,000 square feet of floors!



Questions
