



Facilities Updates
09/22/25

Byrnes High School Phase 3 – Areas G & H



Areas G & H

- Roof steel installation is complete and roofing is in progress
- Overhead utility installation is in progress
- Brick installation is nearly complete on east side – will begin south side this week

Cafeteria Addition

- Roof steel to begin this week
- Air barrier to begin this week with brick installation to follow soon after
- First layer of asphalt has been installed

Byrnes High School Phase 3 – Areas D & F




Area D

- Roofing is complete
- Brick installation is nearing completion
- Window installation will begin this week
- Interior block fill and paint has begun
- Stair installation is complete

Area F

- Roofing installation is in progress
- First floor overhead utilities are in progress

Byrnes High School Phase 3 – Area E

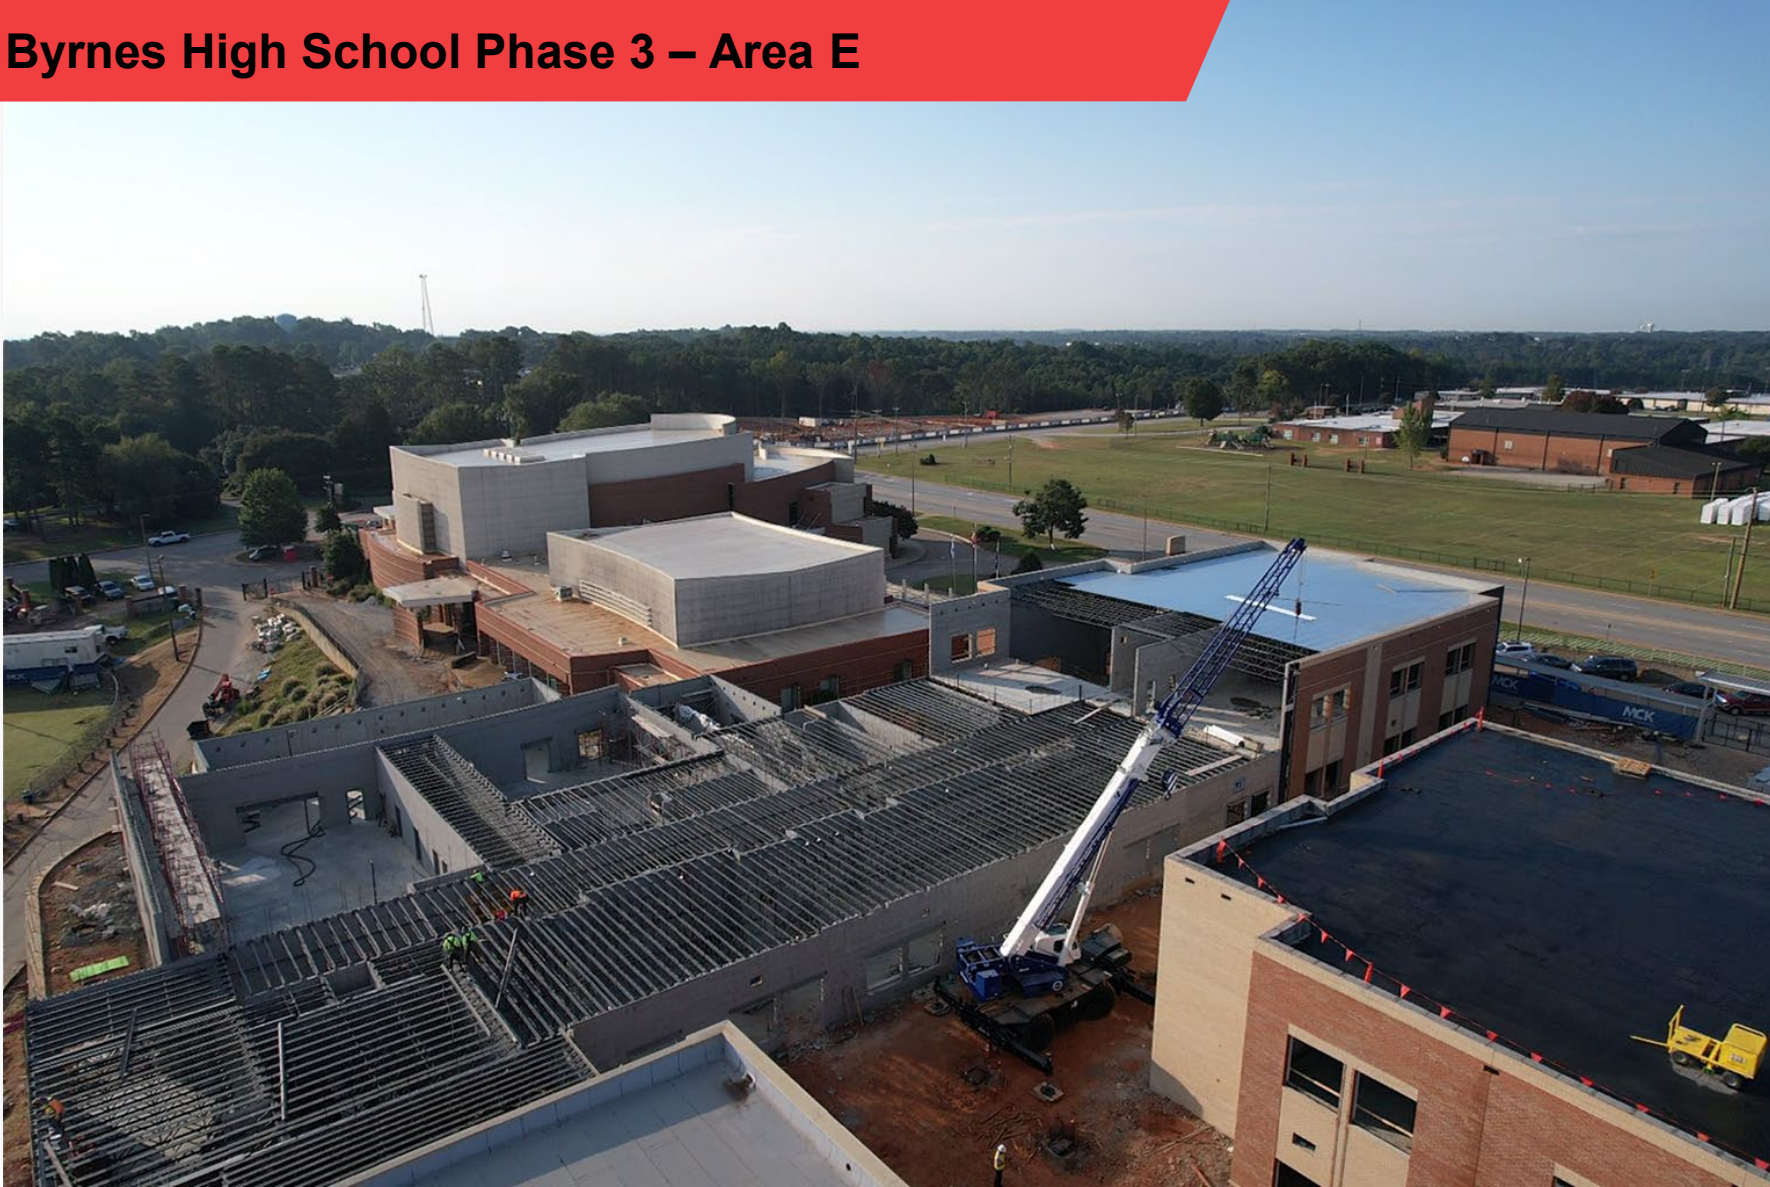

Area E


- Second floor steel framing is complete
- Concrete slab pour is scheduled for next week
- First floor overhead utilities are ongoing
- Brick installation on the retaining wall is ongoing

Schedule is on track

Byrnes High School Stadium



- Track Storage / Spring Sports Locker Room building is complete
- Thompson Turner is working to complete the punch list





Questions
