




Facilities Updates
04/28/25

Byrnes High School Phase 3 – Areas G & H




Areas G & H

- 1st floor masonry walls are complete
- 2nd floor joist install will be complete this week
- Floor slab decking and welding to begin next week
- 2nd floor slab to be poured at the end of May



Byrnes High School Phase 3 – Areas D & F

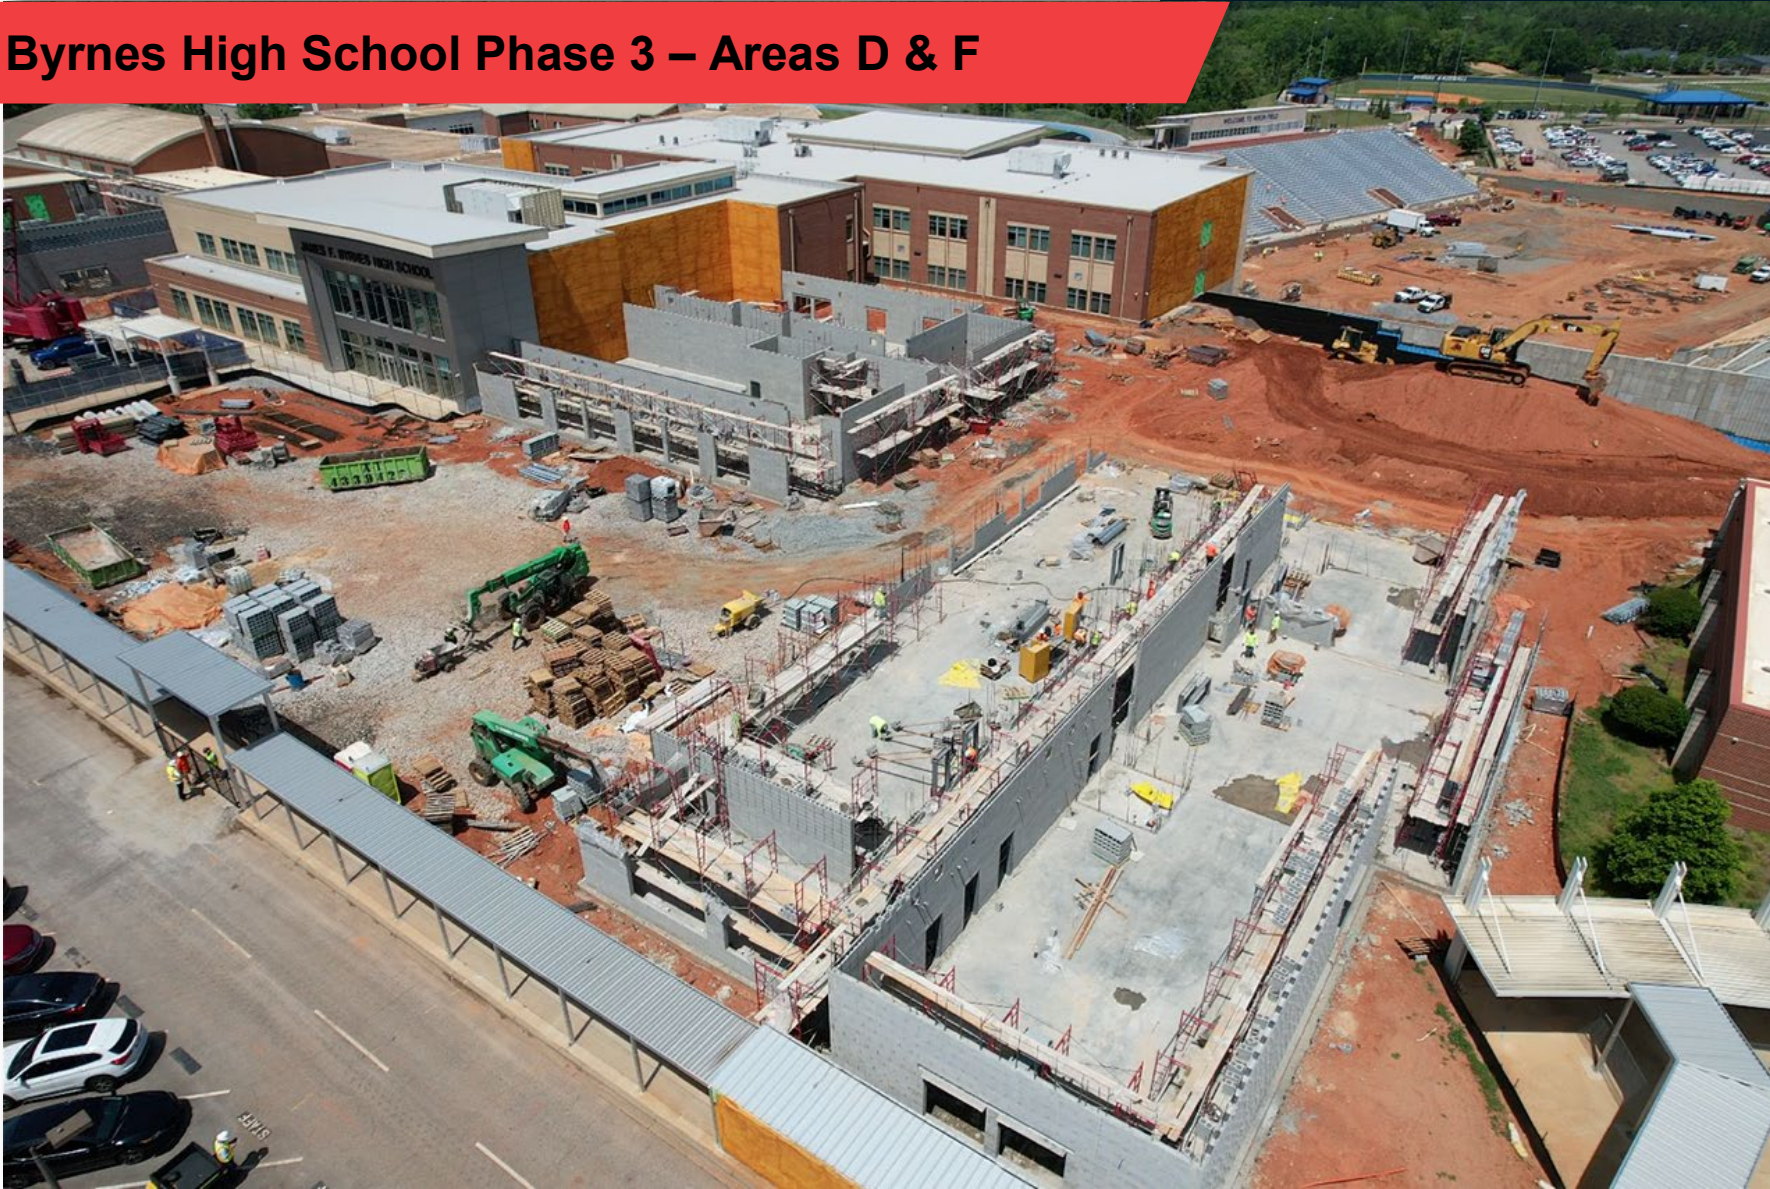


Area D

- 1st floor masonry walls completed last week
- 2nd floor joist install will begin end of next week
- Pour 2nd floor slab at the end of May

Area F

- 1st floor masonry walls will be complete beginning of May
- 2nd floor joist install to begin mid-May




Byrnes High School Phase 3 – Area E



Area E

- Retaining wall is complete
- Waterproofing, storm drain, and backfilling has begun
- Footings tentatively scheduled to begin at the beginning of June


Schedule is on track



Byrnes High School Stadium




- Home bleachers are nearing completion
- Light poles were postponed but are to begin footings soon
- All bleacher field concrete stairs were poured last week
- Field is being cleared and they will begin cutting for underdrains beginning of May
- Turf install to start at the beginning of June



Byrnes High School Stadium



- Press Box dimensional letters are installed
- Entry tunnels are nearing completion
- Scoreboard is installed
- Field Goal netting posts to begin install at the beginning of May




Byrnes High School Stadium



Press Box Building

- Brick is 90% complete
- Top floor stucco finish is complete on field side
- 2nd & 3rd floor drywall is nearing completion
- Exterior windows are 95% complete
- Overhead utilities are 90% complete
- 2nd floor ceiling grid install began last week



Byrnes High School Stadium




Buildings B, C, D

- Received block fill and the first coat of paint
- Ceiling grid install will start in 2 weeks
- Plumbing fixture install will start at end of May

Buildings E

- Masonry walls are topped out
- Joist and decking to begin install at the beginning of May



Byrnes High School Stadium



Building F


- Masonry walls have been topped out
- Joist install is on-going and decking will be installed this week
- In-wall utilities are in progress

Building G

- Ramp retaining walls are complete – footings to begin soon

Visitor bleachers will be complete mid-May

Schedule is on track





Questions
