



Facilities Updates

04/27/26

Beech Springs – Danzler Road Widening Completed



Byrnes High School Phase 3 – Areas G & H



Areas G & H

- Roofing is complete
- Terrazzo is complete on both levels
- VCT install is complete
- Millwork installation is in progress on the first floor
- Plumbing fixture installation is in progress
- Painting is in progress
- Marker and tack board installation is in progress
- Gym flooring installation will begin this week
- Courtyard concrete has been poured
- Cafeteria Addition overhead utility work continues

Byrnes High School Phase 3 – Areas G & H



2nd Floor Level Restroom



West Courtyard

Byrnes High School Phase 3 – Area D



Area D

- Science Lab casework installation is in progress
- Final paint coat is in progress
- East courtyard amphitheater is in progress
- Canopy footings are in progress


Byrnes High School Phase 3 – Areas E & F



Area E & F

- Overhead utilities are in progress
- Second floor painting is in progress
- Heat pump start up begins this week
- Terrazzo prep work began last week on the second floor
- Roofing tie-in to the Band building is in progress
- Metal wall panel installation is in progress
- Asphalt paving on the back drives is complete
- Project is on schedule and budget

Byrnes High School Phase 3 – Front Drive Closure

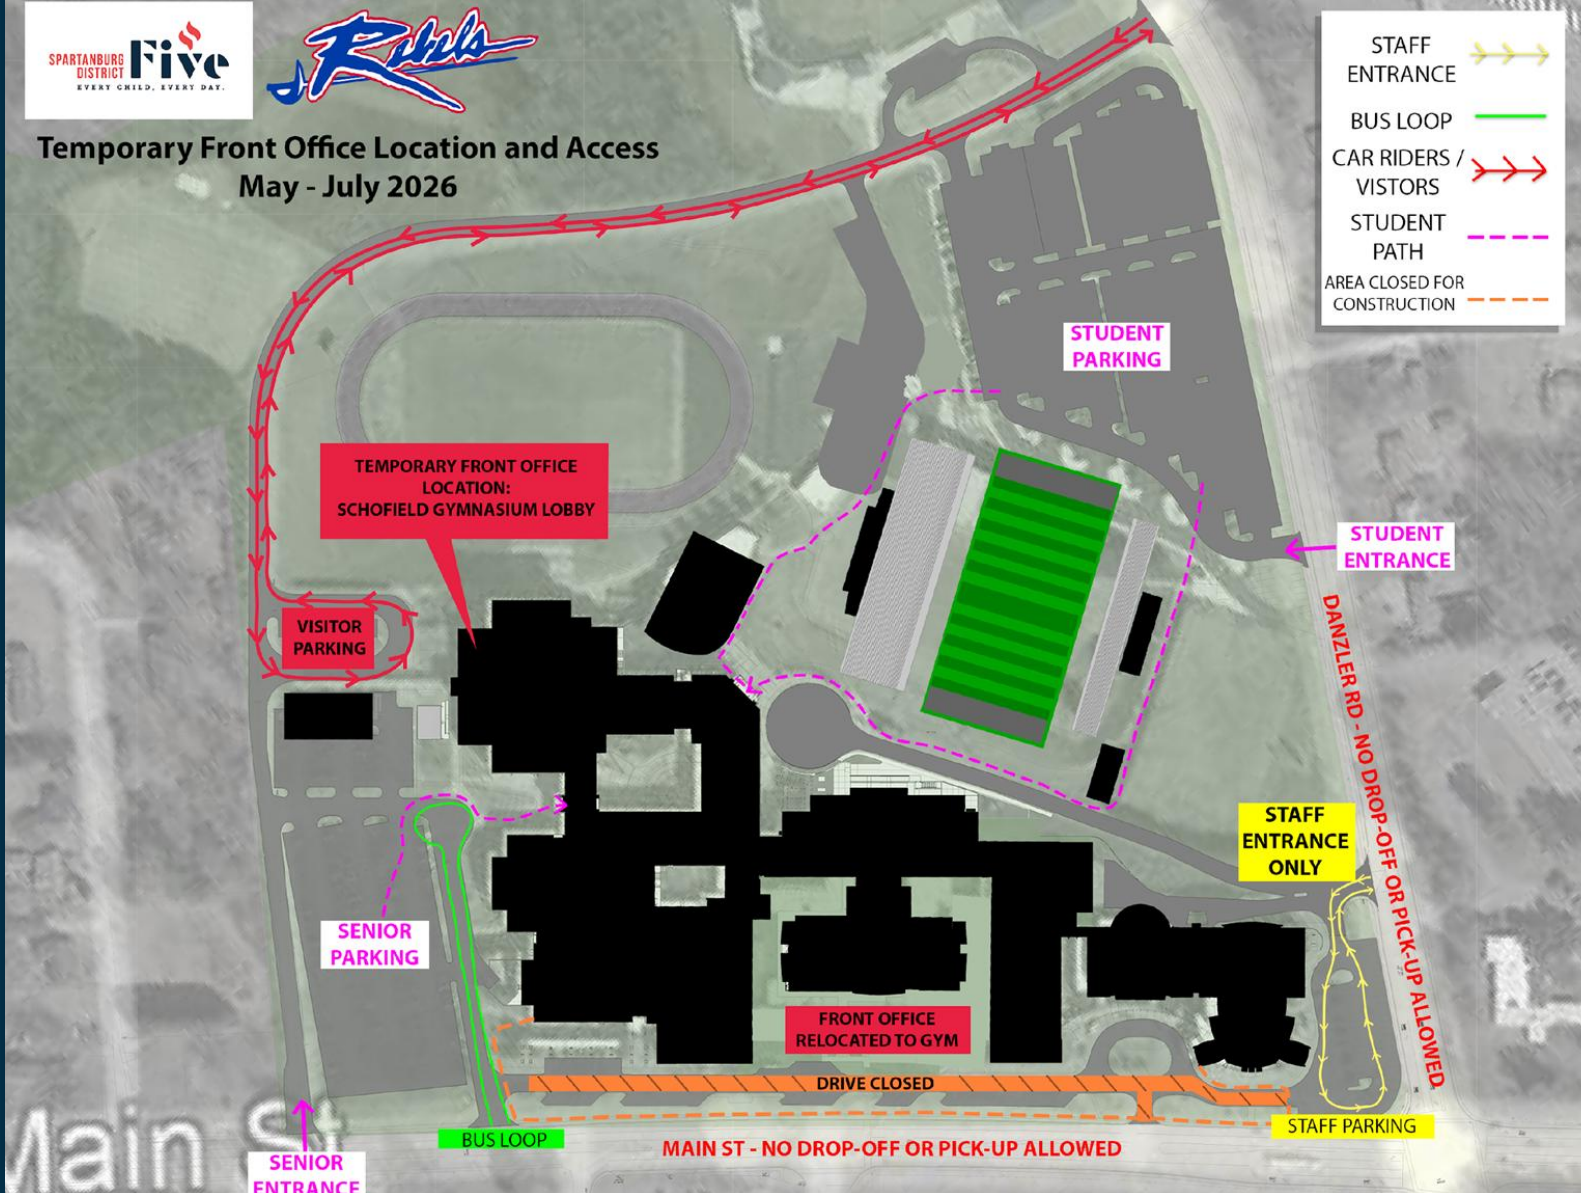

- Front drive will be closed beginning on Sat. May 3rd
- Front office relocates to Schofield Gym Lobby
- Visitor parking will be reserved in front of the gym
- Band students will use the completed back drive to access the band room
- The Fine Arts Center will remain accessible and opened for use
- The FAC parking lot will be open for use beginning on May 5th

South Transportation Center



- Tree clearing began on April 3rd
- Clean up is on-going
- Grubbing and stump removal will begin when we receive the Land Disturbance Permit



Questions
